



PI PLANNING WITH BIGPICTURE



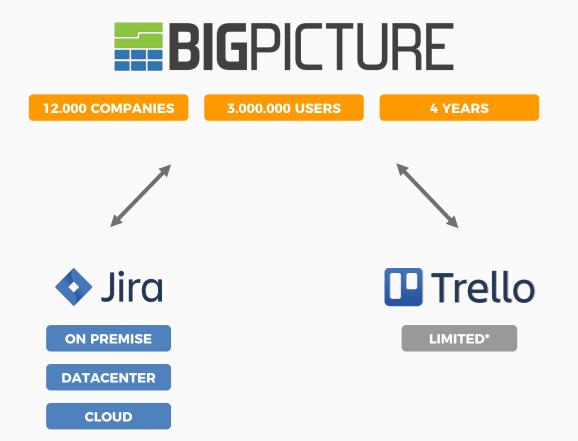


WHAT TOOLS DO YOU NEED TO RUN PI PLANNING EFFECTIVELY?

BIGPICTURE TOOLING PI PLANNING

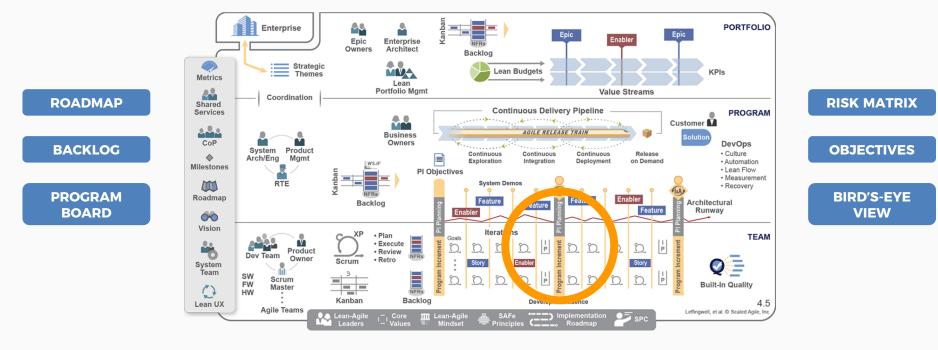


🗙 JIRA Dashboards - Projects - Issues - Boards - BigPic	ture - Create			Search Q 📢 🧭	D- 🗘 🔟 🖓
🚽 SAFe® Summit 2018 Washington, DC	*			Gantt Scope Board Roadmap Resources Teams	Risks 🏚
► Cellt mode 🚓 Teams - ♦ Sort - 🖓 Export 👁 View -	Today Range: 4 -				×
	louay Range. 4 -	Ť			~
SEPTE OCTOBER NOVEMBER		DECEMBER JANUARY		FI FEBRUARY MARCH	APRI >
Program increment 1 27/Sep/18 - 28/Nov/18	CLOSED	Program increment 2 29/Nov/18 - 30/Jan/19	IN PROGRESS-	Program increment 3 1 31/Jan/19 - 03/Apr/19	FORECAST
OBJECTIVES	67%	OBJECTIVES	20%	OBJECTIVES	0%
Sport tracking app for Web - MVP	~	Sport tracking app for iOS - MVP		Support for interval training	
Sport tracking app for Web - MVP	~	Real-time information for users about their running progress (distance and	time) 🗸	Enhanced reporting	
Sport tracking app for iOS - MVP	×	Collecting feedback from users about running autotracking		Support for walking	
Sport tracking app for Android – MVP	\otimes	Self-learning algorithm for running		Support for cycling	
		Autotracking algorithm for running		0	
		0		~	
		v			
Team Android AND					
OBJECTIVES	PBV ABV 50%	OBJECTIVES	PBV ABV 0%	OBJECTIVES	PBV 0%
Tracking, registering, and transferring GPS data to server	0 🗸	Tracking, registering, and transferring GPS data to server	8 0	Android: enhanced reporting	0
Tracking, registering, and transferring GPS data to server	0 ×	Real-time information for users about their running progress (distance an	. 10 3	Android: support for cycling, walking and interval training	0
		Android: Collecting user confirmation on activity type - running	10 0	0	
		0			
Team Smartwatch SMART					
OBJECTIVES	PBV ABV 50%	OBJECTIVES	PBV ABV 0%	OBJECTIVES	PBV 0%
Interface with smartphone	0 🗸	Tracking and registering GPS data	1 4	Smartwatch: enhanced reporting	0
Tracking and registering GPS data	0 ×	Real-time information for users about their running progress (distance an	. 8 0	Smartwatch: support for cycling, walking and interval training	0
		Smartwatch: Collecting user confirmation on activity type - running	5 0	0	
		0		·	
		V			
Zeam Web WEB					
OBJECTIVES	PBV ABV 100%	OBJECTIVES	PBV ABV 0%	OBJECTIVES	PBV 0%
Visualization of tracks on a map	0 🛇	Learning mechanism for identifying running activity	10 0	Algorithm to identify cycling	0
Training log	0 🗸	Algorithm to identify running activity	3 0	Algorithm to identify walking	0
		0		0	

ŸJIRA Dashboards - Projects -	Issues - Boards - BigPicture - Create				Search	٩	r\$ @-	\$≁	- []
SAFe® Summit 201	8 Washington, DC-	Gantt	Scope	Board	Roadmap	Resources	Teams	Risks	۵
🗁 Data 🔻 🐵 View 👻 🖶 Export	$\land \downarrow \leftarrow \Rightarrow \equiv \square Default scope column view * •$				Quick Filters	none		• •	Q
ISSUE TYPE KEY	SUMMARY	ASSIGNEE			STATUS				\$
~ PIV	SAFe® Summit 2018 Washington, DC	🖸 Unas	ssigned						
O Process V PIV-11	Project plan	🖪 admi	in		OPEN				
🗲 Epic 🗸 V PIV-12	Project Management	R admi	in		RESOL	VED			
Story PIV-15	Lead and manage the project team	🖪 admi	in		OPEN				
Story PIV-13	Develop a project plan	🖪 admi	in		OPEN				
Story PIV-14	Establish a project schedule	🖪 admi	in		RESOL	VED			
Fpic V PIV-16	Analysis	🖪 admi	in		IN PRO	GRESS			
Story PIV-18	Gather requirements from business units or users	A admi	in		IN PRO	GRESS			
Story PIV-19	Verify that project deliverables meet the requirements	A admi	in		OPEN				
Story PIV-20	milestone - Document technical and business requirements	A admi	in		OPEN				
Story PIV-1	Gather external opinions on the project	🖪 admi	in		OPEN				
Fpic V PIV-2	Testing	A admi	in		OPEN				
Story PIV-3	Configuring, using, and managing test environments and test data	🖪 admi	in		OPEN				
Story PIV-4	Measuring and reporting test coverage	🖪 admi	in		OPEN				
🛃 Epic 🗸 🗸 PIV-5	Architecture	🖪 admi	in		OPEN				
Story PIV-6	Picking & executing the right modelling	🖪 admi	in		OPEN				
Story PIV-7	Understand and plan for evolutionary paths	🖪 admi	in		OPEN				
Story PIV-8	Identify and interact with stakeholders	🖪 admi	in		OPEN				
Fpic V PIV-9	Operations	🖪 admi	in		OPEN				
Story PIV-10	Planning and controlling of change, resources and deadlines	🖪 admi	in		OPEN				

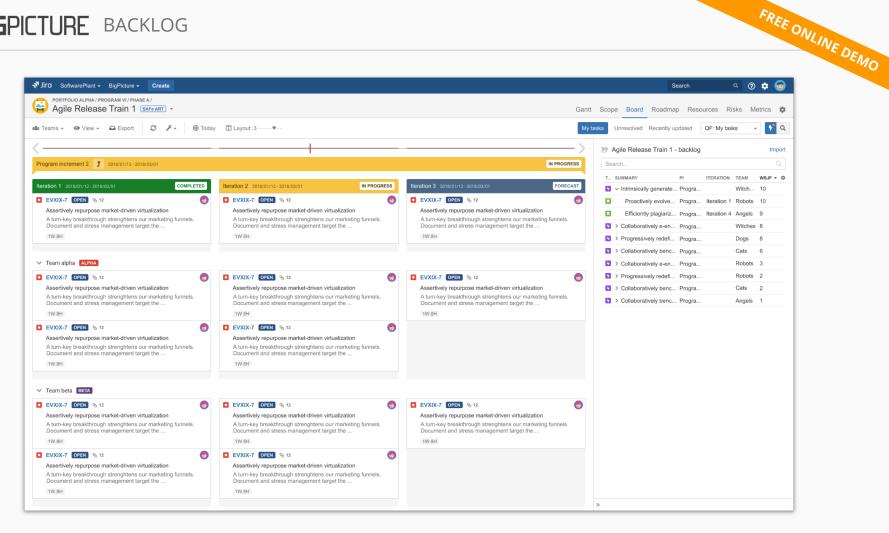

BIGPICTURE DEPENDENCY BOARD

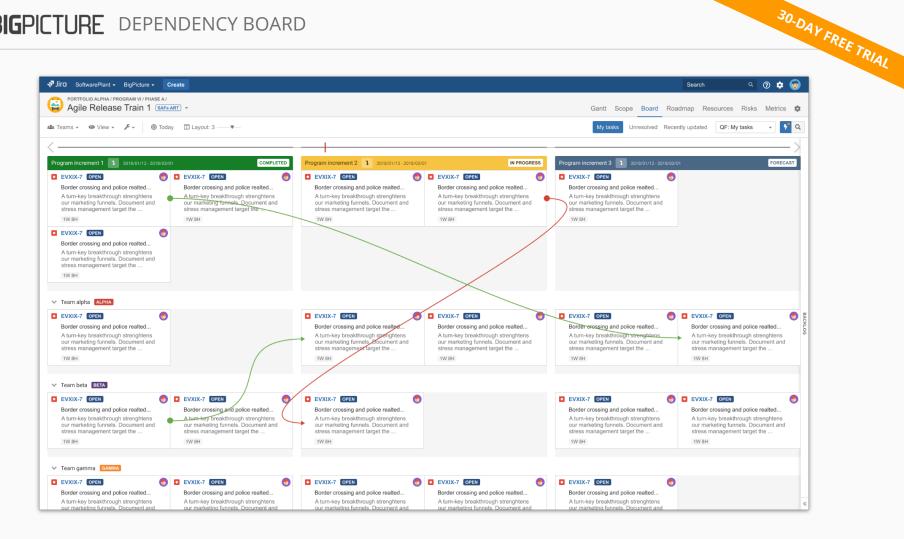

Ϋ́J	IRA Dashboards - Projects - Issues - Boards -	BigPicture - Create						\$* © • \$	• 🛛 •
0	SAFe® Summit 2018 Washington,	, DC-			Gantt S	cope Board F	Roadmap Resources	Teams Rist	s 🌣
+ R	isk 🕶 🐵 View 🔹 💠 Sort 👻 📇 Export					Quick Filters: no	one	· • 🗇	a X
			CONSEQUEN						
	TRIVIAL	LOW	MEDIUM		HIGH PIV-14	П	SE	VERE	
ALMOST NONE	Develop a project plan				Establish a project schedule	P.4			
ALMOS	OPEN				RESOLVED				
	Verify that project deliverables meet the re-		Gather requirements from	business units or					
LOW	quirements OPEN		USERS						
PROBABILITY MEDIUM									
PRO ME									
	PIV-12 R	PIV-15 Lead and manage the project team	PIV-11 Project plan	Я					
HIGH	RESOLVED	OPEN	OPEN						
							9 PIV-16		
VERY HIGH							Analysis		
VE							IN PROGRESS		
IS	SUE TYPE KEY	SUMMARY AS	SIGNEE	STATUS	RISK PROBABILITY	RISK CO	INSEQUENCE		۵
6	·			IN PROGRESS	Very high	Severe		Edit	
			,	OPEN	Almost none	Trivial			Delete
	PIV-14	Establish a project schedule	,	RESOLVED	Almost none	High		Edit	Delete Feedback


	Boards ▼ BigPi				Search Q 📢 🕐 🕈 🕶
SAFe® Summit 2018 Was	hington, DC	•	Gant	tt Scope	Board Roadmap Resources Teams Risks
Edit mode 🔹 Teams 🔹 🗘 Sort 👻 🖾 Exp	oort 💿 View 🗸	◎ Today Range: 4			
SEPTE OCTOBER NOVE	MBER	DECEMBER JANUARY	FEBRUARY MARCH	APRIL	MAY JUNE
rogram increment 1 1 26/Sep/18 - 27/Nov/18	CLOSED	Program increment 2 28/Nov/18 - 29/Jan/19 CLOSED	Program increment 3 30/Jan/19 - 02/Apr/19	N PROGRESS	Program increment 4 1 03/Apr/19 - 04/Jun/19 FORECA
OBJECTIVES	67%	OBJECTIVES 33%	OBJECTIVES	10%	OBJECTIVES
Sport tracking app for Web - MVP	~	Sport tracking app for iOS - MVP ×	> This is my new objective!		Professionally cloudify extensive networks
Sport tracking app for Web - MVP	~	Real-time information for users about their running progress (\checkmark	Sport tracking app for iOS - MVP		Dramatically re-engineer agile interfaces
Sport tracking app for iOS - MVP	×	> Collecting feedback from users about running autotracking ×	> Collecting feedback from users about running autotr	acking	
Sport tracking app for Android MVP	0	Self-learning algorithm for running	Self-learning algorithm for running	~	
		Autotracking algorithm for running	Autotracking algorithm for running		
		✓ This is my new objective! ×	PIV-2 Testing		
		Smartwatch: Collecting user confirmation on activity typ	Support for interval training		
		My new objective!	Enhanced reporting		
		,	Support for walking		
			 Support for cycling 		
			Real-time information for users about their runnin	a progr	
			Android: Collecting user confirmation on activity t		
Team Android AND	PBV ABV 50%	ORJECTIVES PBV ABV 75%	OBJECTIVES F	PBV ABV 0%	
OBJECTIVES					
Tracking, registering, and transferring GPS data	at 0 🗸	Tracking, registering, and transferring GPS data t 8 0 🗸	Tracking, registering, and transferring GPS dat	0	
	at 0 🗸	Tracking, registering, and transferring GPS data t 8 0 ✓ Real-time information for users about their runnin 10 3 ✓	Tracking, registering, and transferring GPS dat Android: Collecting user confirmation on activity	0	
Tracking, registering, and transferring GPS data	at 0 🗸	Tracking, registering, and transferring GPS data t 8 0 ✓ Real-time information for users about their runnin 10 3 ✓ Android: Collecting user confirmation on activity t 10 0 ×	Tracking, registering, and transferring GPS dat Android: Collecting user confirmation on activity Android: enhanced reporting	0 0 0 0	
Tracking, registering, and transferring GPS data	at 0 🗸	Tracking, registering, and transferring GPS data t 8 0 ✓ Real-time information for users about their runnin 10 3 ✓	Tracking, registering, and transferring GPS dat Android: Collecting user confirmation on activity	0 0 0 0	
Tracking, registering, and transferring GPS data Tracking, registering, and transferring GPS data	at 0 🗸	Tracking, registering, and transferring GPS data t 8 0 ✓ Real-time information for users about their runnin 10 3 ✓ Android: Collecting user confirmation on activity t 10 0 ×	Tracking, registering, and transferring GPS dat Android: Collecting user confirmation on activity Android: enhanced reporting	0 0 0 0	
Tracking, registering, and transferring GPS data Tracking, registering, and transferring GPS data	at 0 🗸	Tracking, registering, and transferring GPS data t 8 0 ✓ Real-time information for users about their runnin 10 3 ✓ Android: Collecting user confirmation on activity t 10 0 ×	Tracking, registering, and transferring GPS dat Android: Collecting user confirmation on activity Android: enhanced reporting Android: support for cycling, walking and interv	0 0 0 0	
Tracking, registering, and transferring GPS data Tracking, registering, and transferring GPS data Team Smartwatch	at 0 🗸	Tracking, registering, and transferring GPS data t 8 0 ✓ Real-time information for users about their runnin 10 3 ✓ Android: Collecting user confirmation on activity t 10 0 X My new objective! 10 7 ✓	Tracking, registering, and transferring GPS dat Android: Collecting user confirmation on activity Android: enhanced reporting Android: support for cycling, walking and interv	0 0 0 0 0	
Tracking, registering, and transferring GPS data Tracking, registering, and transferring GPS data Team Smartwatch	at 0 🖍	Tracking, registering, and transferring GPS data t 8 0 ✓ Real-time information for users about their runnin 10 3 ✓ Android: Collecting user confirmation on activity t 10 0 X My new objective! 10 7 ✓ OBJECTIVES PBV ABV e%	Tracking, registering, and transferring GPS dat Android: Collecting user confirmation on activity Android: enhanced reporting Android: support for cycling, walking and interv	0 0 0 0 0 0 0 0 0 0 0	
Tracking, registering, and transferring GPS data Tracking, registering, and transferring GPS data Team Smartwatch SMART OBJECTIVES Interface with smartphone	at 0 ~/ at 0 X PBV ABV 50% 0 /	Tracking, registering, and transferring GPS data t 8 0 ✓ Real-time information for users about their runnin 10 3 ✓ Android: Collecting user confirmation on activity t 10 0 × My new objective! 10 7 ✓ OBJECTIVES PBV ABV 0% Tracking and registering GPS data 1 4 ×	Tracking, registering, and transferring GPS dat Android: Collecting user confirmation on activity Android: enhanced reporting Android: support for cycling, waiking and interv OBJECTIVES Tracking and registering GPS data	0 0 0 0 0 0 0 0 0 0 0	
Tracking, registering, and transferring GPS data Tracking, registering, and transferring GPS data Team Smartwatch SMART OBJECTIVES Interface with smartphone	at 0 ~/ at 0 X PBV ABV 50% 0 /	Tracking, registering, and transferring GPS data t 8 0 ✓ Real-time information for users about their runnin 10 3 ✓ Android: Collecting user confirmation on activity t 10 0 × My new objective! 10 7 ✓ OBJECTIVES PBV ABV PK Tracking and registering GPS data 1 4 × Real-time information for users about their runnin 8 0 ×	Tracking, registering, and transferring GPS dat Android: Collecting user confirmation on activity Android: enhanced reporting Android: support for cycling, walking and interv OBJECTIVES Tracking and registering GPS data Real-time information for users about their runn Smartwatch: Collecting user confirmation on ac	0 0 0 0 0 0 0 0 0 0 0	

BIGPICTURE OBJECTIVES

\bigcirc	Self-learning algorithm for running				Support f
	Autotracking algorithm for running				
	•				
V ABV 50%	OBJECTIVES	ing algorithm for running			
~	Tracking, registering, and transferring GPS data to server	8	0		Android:
×	Real-time information for users about their running progress (distance an	10	3	~	Android:
	Android: Collecting user confirmation on activity type - running	10	0		
	This is my new object			+	
V ABV 50%	OBJECTIVES	PBV	ABV	0%	OBJECTIVES
~	Tracking and registering GPS data	1	4		Smartwat
×	Real-time information for users about their running progress (distance an	8	0		Smartwat

30-DAY FREE TRIAL

BIGPICTURE PROGRAM BOARD

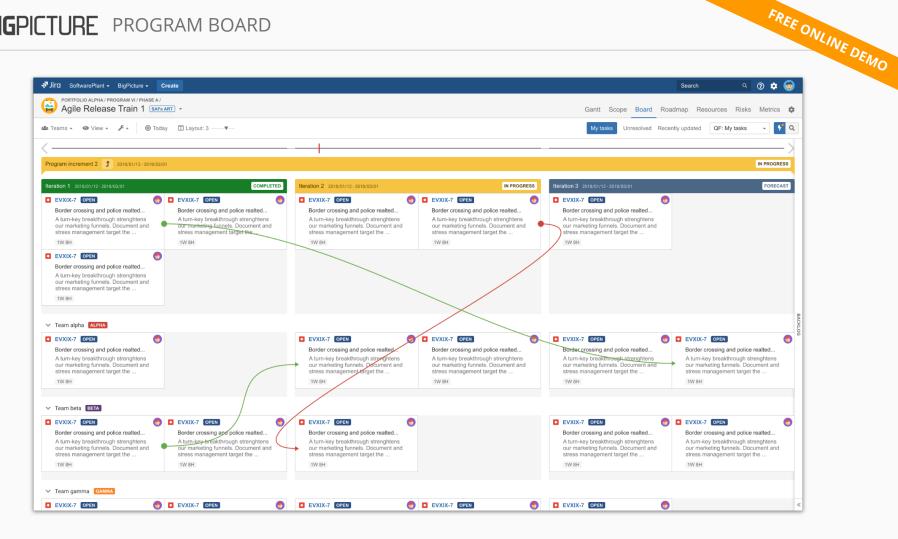

			2 M/aabia	atan DC													
ງ SAFe® Sເ	ILLILL	111 2016	s washin	gion, DC÷							Gantt Scop	e Board	Roadmap	Resources	Teams	Risks	
iduals Teams f	🕞 Skill	ls 🕑 Or	iginal Estimate	• • View • 4	🖹 Export 🛛 👯 S	cale - << <	Today >	>>					Quick	Filters: none		•	
ividuals with tasks		AU		SEPTEMBI 9 10 11 12 13 14 15 16					OCTOBER 2018				NOVEME				
ummary	ίΞ	0	04 05 06 07 08 0 0	9 10 11 12 13 14 15 16 34.1	17 18 19 20 21 22 23 100.1	3 24 25 26 27 28 29 3 92.1	268.9	186.4	4 15 16 17 18 19 20 21 170.3	22 23 24 25 26 27 28 141.7	29 30 31 01 02 03 04 25.6	7.3	0 11 12 13 14 15 7.3	16 17 18 19 20 21	22 23 24 25 77.3	0	í
		24.0	56.0	56.0	56.0	56.0	56.0	56.0	56.0	56.0	56.0	56.0	56.0	,	56.0	32.0	j
Unassigned	ίΞ	0	0	0	0	0	0	0	0	0	0	0	0		0	0	
admin	ίΞ	0	0	34.1	100.1	92.1	268.9	186.4	170.3	141.7	25.6	7.3	7.3		77.3	0	Ē
111.1/728.0 D P		24.0	56.0	56.0	56.0	56.0	56.0	56.0	56.0	56.0	56.0	56.0	56.0	,	56.0	32.0	j
				PIV-12 - Project Mar PIV-13 -	PIV-5 - Architectu		PIV-2 - Testing		PIV-9 - Operations PIV-16 - Analys	is							
				PIV-14 - Establish a		- Lead and	PIV-3 - Configuring,		PIV-10 - Planning a	and controlling					Loud		
					PIV-6 - Picking &	PIV-7 - Unde	PIV-4 - Measuring ar	PIV-8 - Identify a	PIV-18 - Gathe						PIV		
								ther external opinions (PIV-19 - Verify	that						
vills		AU		SEPTEMB	ER 2018			c	OCTOBER 2018				NOVEME	3ER 2018			
				9 10 11 12 13 14 15 16		3 24 25 26 27 28 29 3		08 09 10 11 12 13 1	10 10 11 10 10 10 11	22 23 24 25 26 27 28		05 06 07 08 09 1		16 17 18 19 20 21) 3
Immary		0 24.0	0	32.0	87.2 56.0	101.7	247.9	199.0	161.0 56.0	156.8	32.7	7.1 56.0	7.1		79.1 56.0	0	1
Unspecified		0	0	32.0	87.2	101.7	247.9	199.0	161.0	156.8	32.7	7.1	7.1		79.1	0	ł
onspecified		0	0	0	0	0	0	0	0	0	0	0	0		0	0	1
Developer		0	0	0	0	0		0	î . î	0	0	0	0		0	0	î
		12.0	28.0	28.0	28.0	28.0	28.0	28.0	28.0	28.0	28.0	28.0	28.0		28.0	16.0	j
Project Manager	ίΞ	0	0	0	0	0	•	0		0	0	0	0		0	0	ľ
		12.0	28.0	28.0	28.0	28.0	28.0	28.0	28.0	28.0	28.0	28.0	28.0		28.0	16.0	1

30-DAY FREE TRIAL

Ä	Jira	Dashboards - Projects	- Issues -	Boards - BigPic	ture - Create									Search	٩	\$1 0	• \$ •	10-
0	😝 S/	AFe® Summit 20)18 Wash	ington DC-							Gantt	Scope	Board	Roadmap	Resources	Teams	Risks	¢
+	• Task 👻	🗁 Data 🗸 💿 View 🗸	🙁 Resource	es 🖉 Export	HHI 👻 🚺	+ + ·		→ / □					Quick Filters	: none	•	Image: Contract of the second seco	۹ م	×
ΥP	E KEY	SUMMARY	STATUS	REPORTER	TIME TRACKING[Σ] STORY POINTS[21 22 23 24 25 26 27 28 29 30 31 01 02 03	04 05 06 07 08 09 10 11	September, 2018 12 13 14 15 16 17 18	19 20 21 22 23	24 25 26 27	28 29 30 01	02 03 04 05 06 0	7 08 09 10 11 12 1	October, 20 3 14 15 16 1		1 22 23
	INITIAT	Iv - Initiative 3	TO DO	Mike Brooks	0%	•			INITIATIVE-3 - Initiativ	e 3								
-	INITIAT	Initiative 2	TO DO	Mike Brooks	78%	93% 4% 3	2											
୭	INITIAT	Capability 1	TO DO	Mike Brooks	0%	320			INITIATIVE-4 - Capability 1									
0]	INITIAT	Capability 2	TO DO	😰 Mike Brooks	78%	53% 26%	2											
,	PII-2	- Testing	IN PROGRESS	🗧 📵 Mike Brooks	88%	25% 42%	3											
3	PII-4	- Measuring and	OPEN	Mike Brooks	98%	9			РШ	4 - Meası								
1	PII-3	- Configuring, u	sir IN PROGRESS	🗧 📵 Mike Brooks	68%	15		PII-3 -	Configuring, using, and mar	aging test environment	s and test data							
3	PII-14	Establish a pro	oj∈ CLOSED	Mike Brooks	74%	12		PII-14 - Establish a project scher										
1	PII-5	- Architecture	OPEN	Mike Brooks	75%	100% 0%												
]	PII-6	Picking & exec	OPEN	Mike Brooks	90%	•			Ріі-	5 - Picking & executing	he right modelling		η					
	PII-7	Understand an	OPEN	Mike Brooks	80%	21									PII-7 - Unde	erstand and pl	an for evolutio	bnary pa
]	PII-8	Identify and in	ter OPEN	Mike Brooks	27%													
•	PII-9	Operations	OPEN	😻 Mike Brooks	68%	0% 0% 0%												
3	PII-10	Planning and	OPEN	Mike Brooks	36%							PII-10 - P	anning and co	ntrolling of change	resources and dear	dlines 🖊		
			RES	OURCES			20	21 22 23 24 25 26 27 28 29 30 31 01 02 03	04 05 06 07 08 09 10 11	September, 2018	19 20 21 22 23	24 25 26 27	28 29 30 01	02 03 04 05 06 0	7 08 09 10 11 12 1	October, 20		1 22 23
4	Chris M	Manzini							21 16	40 40								
(5 Kathy	Donovan							7 1									
(🕑 Mike B	Brooks					6	6 6 14 14 14 23	19 19 48	48 45 46	46	46 31 31	21	21 21	29 29 29	29 32 3	2	32 41
F	Unass	igned															See	edback

